










ID	Task Name	Duration	Start	Finish	2001												2002					
					Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
110	- reflector assembly	80 days	Tue 8/15/00	Thu 11/30/00																		
111	- rebuild cabin	40 days	Mon 1/8/01	Wed 2/28/01																		
112	- to pad at Haystack (tests)	12 days	Mon 3/5/01	Tue 3/20/01																		
113	- ship from Haystack	13 days	Tue 4/3/01	Thu 4/19/01																		
114	- ship from Seattle to HNL	12 days	Fri 4/20/01	Mon 5/7/01																		
115	- ship HNL to KAW	5 days	Tue 5/8/01	Mon 5/14/01																		
116	- arrive MK	0 days	Mon 5/14/01	Mon 5/14/01																		
117	- fitout	35 days	Tue 5/15/01	Mon 7/2/01																		
118	- reflector on mount 5	5 days	Thu 6/7/01	Wed 6/13/01																		
119	- install receiver	3 days	Thu 6/14/01	Mon 6/18/01																		
120	- antenna 5 to pad	1 day	Tue 7/3/01	Tue 7/3/01																		
121																						
122	<b>Antenna 6</b>	<b>201 days</b>	<b>Wed 4/4/01</b>	<b>Wed 1/9/02</b>																		
123	- reflector assembly	50 days	Mon 7/23/01	Fri 9/28/01																		
124	- chopping secondary	80 days	Mon 9/3/01	Fri 12/21/01																		
125	- mount assembly	125 days	Wed 4/4/01	Tue 9/25/01																		
126	- ship from Haystack	13 days	Wed 9/26/01	Fri 10/12/01																		
127	- ship from Seattle to HNL	15 days	Wed 10/17/01	Tue 11/6/01																		
128	- ship HNL to KAW	5 days	Wed 11/7/01	Tue 11/13/01																		
129	- arrive MK	0 days	Tue 11/13/01	Tue 11/13/01																		
130	- fitout	40 days	Wed 11/14/01	Tue 1/8/02																		
131	- reflector on mount 6	5 days	Mon 12/17/01	Fri 12/21/01																		
132	- install receiver	3 days	Mon 12/24/01	Wed 12/26/01																		
133	- antenna 6 to pad	1 day	Wed 1/9/02	Wed 1/9/02																		
134																						

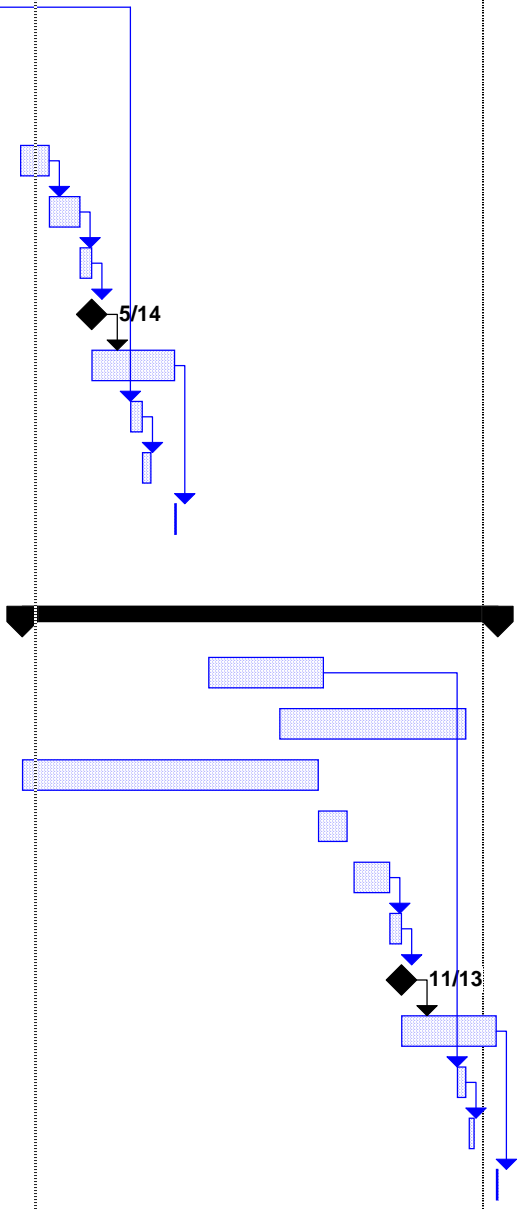



ID	Task Name	Duration	Start	Finish	2001												2002									
					Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
160																										
161	<b>Rebuild cabin on Antenna 2</b>	<b>102 days</b>	<b>Tue 6/11/02</b>	<b>Wed 10/30/02</b>																						
162	- move into hanger	1 day	Tue 6/11/02	Tue 6/11/02																						
163	- remove old fixtures	10 days	Wed 6/12/02	Tue 6/25/02																						
164	- azimuth bearing swap	15 days	Wed 6/26/02	Tue 7/16/02																						
165	- mount modifications	15 days	Wed 7/17/02	Tue 8/6/02																						
166	- fit new cabin	20 days	Wed 8/7/02	Tue 9/3/02																						
167	- install IO box, servo, cabling	35 days	Wed 9/4/02	Tue 10/22/02																						
168	- refit rx	5 days	Wed 10/23/02	Tue 10/29/02																						
169	- move to pad	1 day	Wed 10/30/02	Wed 10/30/02																						

